



**Project:** Elida Local Schools

**Week of:** 07/13/2020

**PROJECT TEAM**

Owner: .....Elida Local Schools .....  
Architect: .....Garmann/Miller .....  
Construction Manager: .....Peterson Construction Company .....

**FUTURE MEETING DATES**

Date	Time	Location	Topic
07-20-2020	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
07-20-2020	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
07-15-2020	1000hrs	Elida District Office	Core Meeting

**PROGRESS UPDATE**

**Activities Taking Place This Week:**

- CMU being installed in Units B, C and D
- Floor pour prep for the kitchen is taking place
- Electrical, Mechanical and Plumbing in wall rough where needed
- Precast topping pour has taken place in Unit B
- Steel installation detailing continues in A
- Bacteria test on water took place this week

**Planned Activities for Next Week:**

- Concrete floor pour in kitchen will take place
- CMU will continue in Units B, C and D
- Electrical and plumbing to follow masons
- Electric panels will start to be mounted where available
- Roof blocking will start
- Steel detailing will continue and will start in C and D


**PROJECT ISSUES AND ACTION PLAN**

Issue	Date Needed	Action
-------	-------------	--------

1. None currently



Veneer mock up work is taking place in order to be reviewed.

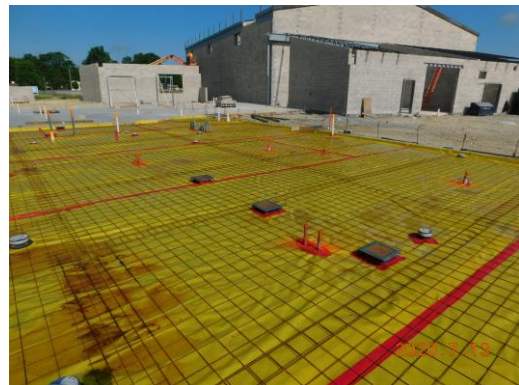

Kitchen floor prepped for concrete pour this week.

**PHOTOS**



Mezzanine above student dining with concrete topping poured



Concrete floor poured on the stage



Steel detailing taking place along gym (angle iron is for roping off while work takes place)



Unit D 1<sup>st</sup> floor North exterior wall complete



Unit C south exterior wall being completed



Hydrant flushing for water bacteria test
