



Project: Elida Local Schools

Week of: 07/27/2020

PROJECT TEAM

Owner:Elida Local Schools
Architect:Garmann/Miller
Construction Manager:Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
08-03-2020	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
08-03-2020	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
08-19-2020	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:


- CMU being installed in Units B, C and D
- Floor pour prep for the gym
- Electrical, Mechanical and Plumbing in wall rough where needed
- Steel installation is taking place in Unit C and D
- Wood blocking is taking place in Unit A
- Kitchen walls are starting

Planned Activities for Next Week:

- Concrete floor pour in gym
- CMU will continue in Units B, C and D
- Electrical and plumbing to follow masons
- Electric panels will continue
- Roof blocking will continue where available
- Steel installation in C and D will continue
- Concrete prep and pour the 2nd floor of C and D

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		

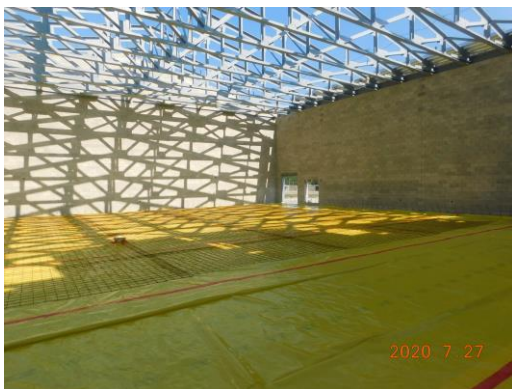

Floor prep taking place for the gym floor concrete pour



Steel beam installed at the A – B connector

PHOTOS



Steel decking installed above the Unit C corridor



Bar Joist installation in the Unit D classroom wing



Steel decking installed above the Unit C classrooms



Masonry walls of the kitchen are being installed



View of the administrative area from the South- looking North



Unit C "Hub" walls being completed in preparation for steel joists
