



Project: Elida Local Schools

Week of: 12/7/2020

PROJECT TEAM

Owner:Elida Local Schools
Architect:Garmann/Miller
Construction Manager:Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
12-14-2020	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
12-14-2020	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
12-16-2020	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units C, D, E and F 2nd floor
- Window installation continues in Units C, D and E
- Metal wall panels continue, roof panels will start
- Metal studs are being installed on 2nd floor classroom wings
- Veneer work continues at E and F
- Electric rough in continues in D, E and F 2nd floor
- Overhead plumbing drains continue

Planned Activities for Next Week:

- Veneer will continue for Units E and F
- Glass installation will continue in Unit C, D and E
- MEP above ceiling on the 2nd floor classroom wings continues
- Paint in available rooms will continue
- Metal roof panels will continue
- Interior masonry walls will continue
- MEP in wall rough continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Scaffold being set up for the main entrance veneer installation



Veneer being completed on the south side of Unit E classroom wing


PHOTOS




Equipment pads installed on the North side of the gym for the mechanical yard area



Metal wall panel installation continues on the West side of the gym

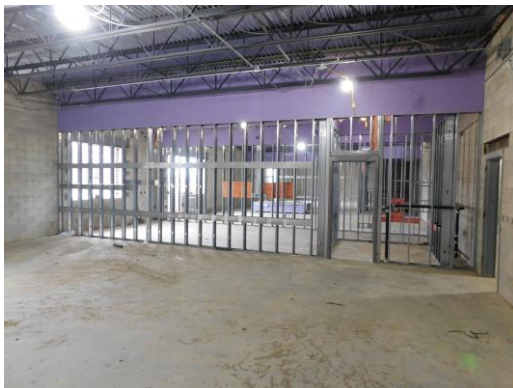

Metal studs and drywall tops installed in the classroom wings

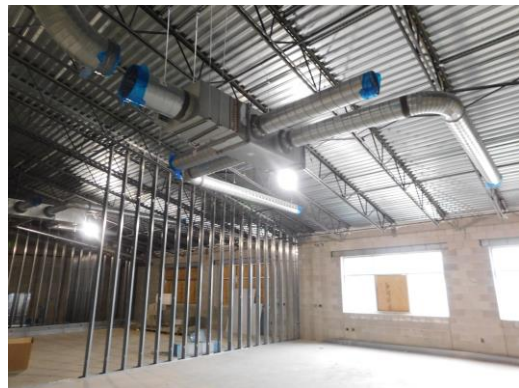

HVAC equipment installation in the classroom wings



Electrical equipment installation in Unit C



Paint started in the Unit A Mechanical Room
