



Project: Elida Local Schools

Week of: 09/28/2020

PROJECT TEAM

Owner:Elida Local Schools
Architect:Garmann/Miller
Construction Manager:Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
10-05-2020	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
10-05-2020	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
10-21-2020	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units A and B
- Gym roof concrete pours are complete
- Drywall top in the admin area has started
- Unit E and F concrete pour for the 2nd floor is scheduled for this week
- Veneer work continues at A, B and C
- Stairs are being worked on in Unit C
- Overhead plumbing drains continue

Planned Activities for Next Week:

- Veneer will continue for Units A, B and C
- CMU will continue in Unit C and D 2nd floor
- Drywall installation at the tops of wall in Admin will continue
- Roof dry in will continue
- Insulation and Z furring for the metal panels will take place
- Concrete pour over the Unit E will be prepped and poured
- Ductwork installation continues
- MEP in wall rough continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



2nd pour took place last week for the gym roof



Day 2 gym roof pour completed last week


PHOTOS




2nd floor of Unit E being prepped for the concrete pour this week.



Unit D bearing walls at corridor and south wall are now at bearing height.

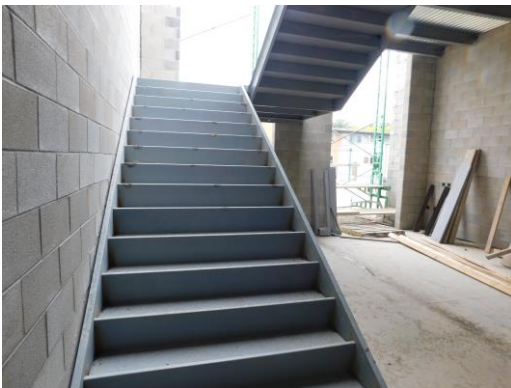

Unit C metal stairs being completed

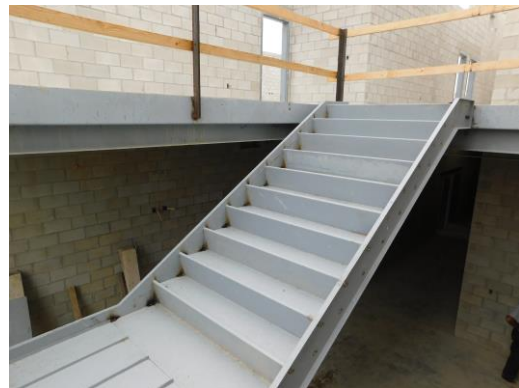

Unit C metal stairs from the landing looking to the 2nd floor



Stone being installed at the main entrance of the building



Veneer completed at the south side of the stage

PHOTOS



Veneer work taking place on the North side of the gym




Veneer almost complete at the east side of the student dining



Insulation and Z furring installed on the east side of the gym roof for the metal panels



Ductwork has started in the media center

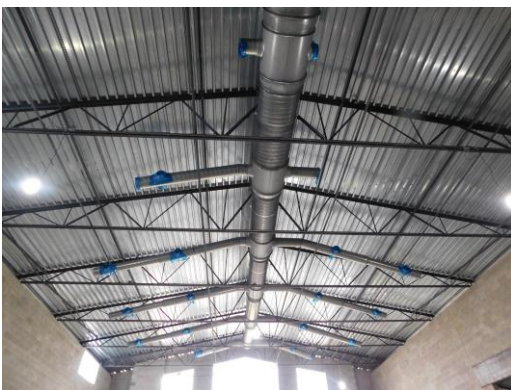

Ductwork continues in the student dining



Drywall tops being installed in the admin area where roof is dried in
